BELLOMASSI

SCOPE AND PLANNING

Scope and Phase Plan

Bellomassi Order-to-Delivery Management Platform

Document ID BM-PLN-001

Document control

Field	Value
Document title	Scope and Phase Plan
Document ID	BM-PLN-001
Version	1.0
Status	Draft — for client review
Category	Scope and Planning
Related module(s)	All modules
Document owner	Project Manager
Prepared by	Project documentation team (AI-assisted draft prepared from source-code analysis)
Reviewed by	*Pending — not yet reviewed*
Approval	*Not approved — awaiting client review (no approval has been given)*
Created date	2026-11-12
Last updated date	2026-11-12

> **Status labels used in this document:** VERIFIED (confirmed in the current source code or existing documents) · PROTOTYPE (works in the React/LocalStorage prototype with mock or simulated behaviour) · PROPOSED (recommended production design, not built) · PENDING CONFIRMATION (needs a client decision) · NOT IMPLEMENTED · NOT VERIFIED.

Purpose

Translate the scope into a phase plan with entry / exit criteria and indicative durations.

Scope

Phase 1 (prototype, complete) to Phase 5 (enhancements). Durations and dates are estimates based on assumptions; no dates have been agreed with the client.

Definitions

Other terms: see **BM-GLO-001** (Project Glossary).


References

- **BM-SOW-001** (Scope of Work)
- **BM-PLN-002** (Phase-wise Scope Matrix)
- **BM-PM-001** (Project Plan)
- **BM-RMP-001** (Prototype-to-Production Migration Roadmap (Master))

1. Phases

Phase	Objective	Main scope	Entry criteria	Exit criteria	Indicative duration (estimate)
1 Prototype	Validate workflows	React / LocalStorage prototype — **complete**	—	Client demo; documentation review	Done
2 Backend	Production core	Django API, PostgreSQL, auth / RBAC, SOW workflows server-side, web app integration	Scope baseline signed; hosting decided	API + web pass system tests in test env	12–14 weeks
3 Mobile and integrations	Field and customer channels	React Native Drivers App, GPS + WebSockets, Maps / Routes, SMS / WhatsApp, email	Phase 2 API stable; provider accounts	Pilot-ready build; integration tests pass	10–12 weeks (overlaps phase 2 by ~4 weeks)
4 Production deployment	Go-live	Security hardening, performance tests, data migration, UAT, training, go-live, hypercare	Phases 2–3 complete	UAT signed; go-live checklist complete	6–8 weeks
5 Enhancements	Stage 2	SAP integration; confirmed extensions; analytics	Go-live stable	Per change request	To be estimated

2. Indicative timeline — ESTIMATE (assumed start date 4 January 2027, not agreed)

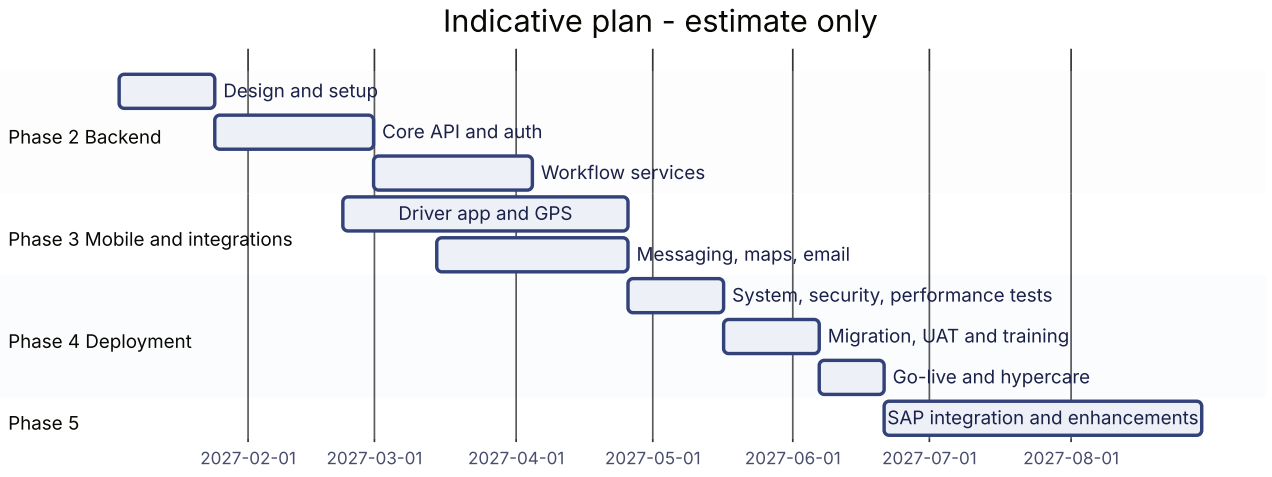

3. Decision gates

Gate	Decision needed	Owner
G0	Approve BRD and SOW scope (extensions X-01 … X-11)	Client sponsor
G1	Hosting, providers (maps, messaging, email)	Client IT
G2	Pilot go / no-go after driver pilot	Logistics owner
G3	Go-live	Steering committee

Phase assignment of every requirement: **BM-PLN-002** (Phase-wise Scope Matrix).

Revision history

Version	Date	Author	Description
1.0	2026-11-12	Documentation team	Initial draft prepared from analysis of the bellomassi-premium-ui source code and existing project documents.
